

II. FISCAL IMPACT ANALYSIS

A. Five Year Summary of Fiscal Impact:

Fiscal Years	2024	2025	2026	2027	2028
Capital Expenditures	-0-	-0-	-0-	-0-	-0-
Operating Costs	-0-	-0-	-0-	-0-	-0-
External Revenues	-0-	-0-	-0-	-0-	-0-
Program Income (County)	-0-	-0-	-0-	-0-	-0-
In-Kind Match (County)	-0-	-0-	-0-	-0-	-0-
NET FISCAL IMPACT	-0-	-0-	-0-	-0-	-0-
# ADDITIONAL FTE					
POSITIONS (Cumulative)	-0-	-0-	-0-	-0-	-0-

Is Item Included in Current Budget? Yes No
 Is this item using Federal Funds? Yes No
 Is this item using State Funds? Yes No

Budget Account No:

Fund Dept Unit Object

Recommended Sources of Funds/Summary of Fiscal Impact:

**This item has no fiscal impact.

Note: Change Order No. 3 to the contract with R&D Paving LLC dated September 13, 2022 (R2022-0914) (Contract) for a time extension of 201 days for Lyons Road/ Sansbury's Way Buffered Bike Lanes project.

C. Departmental Fiscal Review: Danny Rantalsu

III. REVIEW COMMENTS

A. OFMB Fiscal and/or Contract Dev. and Control Comments:

Marc Cough 7/9/24
DA 719 OFMB JTT 7/9

Trinda Grackel 7/10/24
Contract Dev. and Control
Tad 7/10/24

B. Approved as to Form and Legal Sufficiency:

MSS 7/10/24
Assistant County Attorney


C. Other Department Review:

Department Director

This summary is not to be used as a basis for payment.

LYONS ROAD/SANSBURY'S WAY BUFFERED BIKE LANES - FEDERALIZED

PROJECT NUMBER 2019604

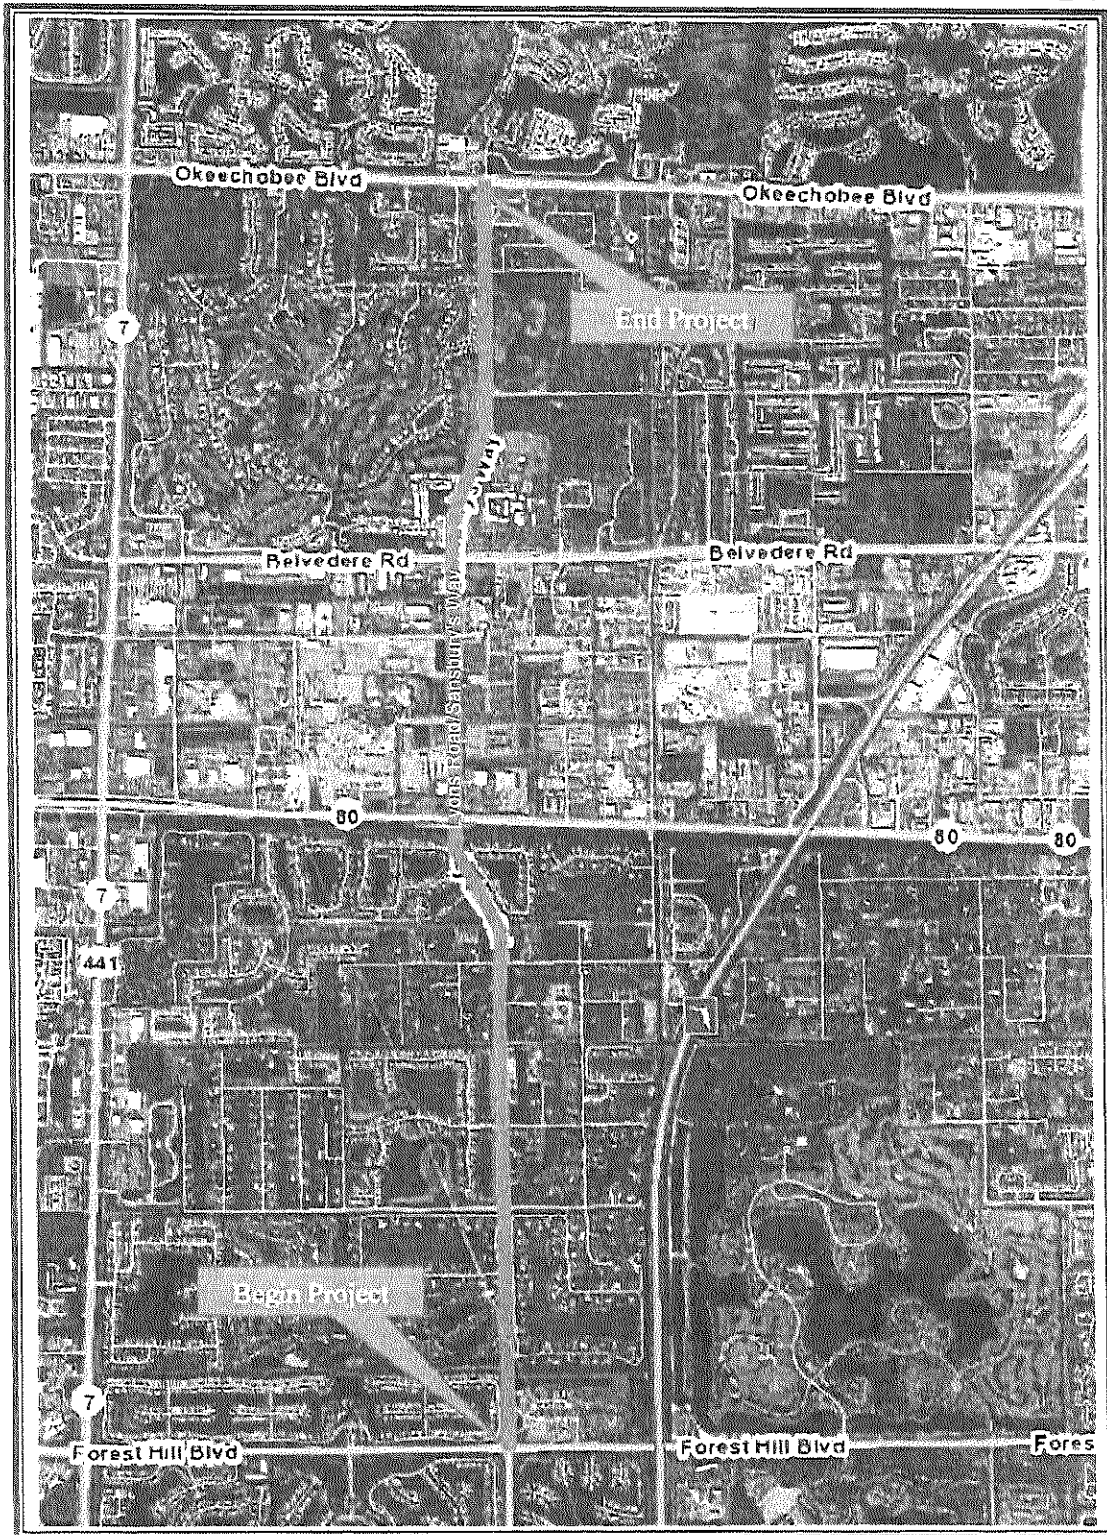

LOCATION MAP



**PALM BEACH COUNTY BOARD OF COUNTY COMMISSIONERS
ENGINEERING & PUBLIC WORKS DEPARTMENT
P. O. BOX 21229, WEST PALM BEACH, FL 33416-1229**

REQUEST:

- WORK ORDER NO. _____
- NEW AUTHORIZATION
- CHANGE ORDER NO. 3
- SUPPLEMENTAL NO. _____
- OTHER: _____

REQUESTING DIVISION:

- ROAD & BRIDGE
- TRAFFIC
- ROADWAY PRODUCTION
- CONSTRUCTION COOR.
- STREETScape

INFORMATION:

DATE: 2/28/2024
 REQUESTOR: Zachary Kim
 COMMISSION DISTRICT NO: 2 & 6
 RESOLUTION NO: R2022-0914
 PBC PO NUMBER: _____

PROJECT LOCATION/LIMITS: Lyons Road/Sansbury's Way Buffered Bike Lanes Federalized FM#44370-1-58-01

PROJECT NUMBER: 2019604
CONTRACT NO: _____

BUDGET LINE ITEM: 3500-361-1908-6551
CONTRACT DATE: September 13, 2022

CONTRACTOR/CONSULTANT/VENDOR: R&D Paving
CONTACT: Matt Dannel

VENDOR: _____
CONTACT PHONE NUMBER: 561-588-6681

Details: Change Order No. 3 will provide a 201-day contract time extension due to delays procuring 8-inch and 4-inch force main materials and an unforeseen Verizon conduit conflict with the proposed drainage. Per specification 8-7.3.2 of the contract, the contractor promptly started the procurement process for the force main materials. Due to the pandemic-induced supply chain challenges, the manufacturer was unable to fulfill the order on time. This delay was beyond the control of both the manufacturer and the contractor and caused a delay in the progress of a critical aspect of the project.

Attachment "A" - Change Order Details
Attachment "B" - EBO Schedules - N/A

Attachment "C" - Certificate of Insufficiency
Attachment "D" - Change Order History

The total amount of this request, per the attached documentation, is not to exceed \$0.00

The Contractor's proposed Small Business Enterprise (SBE) goal for this project was n/a %.
 The estimated SBE participation for this request is n/a %.
 The cumulative SBE participation to date for this contract including this request is: n/a %.

The Minority/Women Owned Business Enterprise (M/WBE) for this contract is n/a %.
 The estimated M/WBE participation for this request is n/a %.
 The cumulative M/WBE participation to date for this Contract including this request is n/a %.

Palm Beach County Engineering and Public Works Contact:

<u>Albert W. Hoffman</u>	<u>Director, Construction Coordination</u>	<u>561-684-4180</u>
Name	Title	Telephone Number

CONTRACTOR/CONSULTANT/VENDOR APPROVALS
 Please indicate your receipt of this request by signing and returning this original document to our office.

ENGINEER OF RECORD (if applicable)

[Signature] 6/4/24
 Signature Date
Nancy G. Russo, Managing Member
 Print Name and Title

 Signature Date

 Print Name and Title

PALM BEACH COUNTY APPROVALS

BOARD APPROVAL? YES Date: August 20, 2024

[Signature] 6/18/24
 Division Approval Date
[Signature] 07/08/2024
 Deputy County Engineer Date

[Signature] 06/17/2024
 Budget Approval Date

 PBC Board of Co. Commissioner Date

ATTEST: Joseph Abruzzo,
 Clerk of the Circuit Court
 & Comptroller

 (Deputy Clerk) Date

Approved as to Form and Legal Sufficiency:
[Signature] 7/15/24
 (County Attorney) Date

CHANGE ORDER

- Owner Initiated _____
- Differing Site Conditions _____
- Zoning/Code/Ordinance Changes _____
- Errors/Omissions/In Design _____

- Quantity Overruns/Underruns
- Request By Another Agency/Outside Party:
- A. Reimbursable B. Non-Reimbursable
- Other: _____

PROJECT: Lyons Road/Sansbury's Way Buffered Bike Lanes
 Federalized
 TO: R&D Paving, LLC

CHANGE ORDER NO: Three (3)
 COUNTY PROJECT NO: 2019604
 CONTRACT DATE: September 13, 2022
 RESOLUTION NO: R2022-0914
 DISTRICT NO: 2 and 6

You are directed to make the following changes in this Contract:

Per FDOT Specification 8-7.3.2 "Contract Time Extensions"

1. Contract Time Extension for Force Main Material Procurement - 99 Days
2. Contract Time Extension for Verizon/ Proposed Drainage Conflict - 102 Days

Contract time extension - 201 days

The original Contract Sum was	\$ 5,862,084.91
Net change by previous Change Orders	\$ 5,647.47
The Contract Sum prior to this Change Order was	\$ 5,867,732.38
The Contract Sum will be unchanged by this Change Order	\$ 0.00
The new Contract Sum including this Change Order will be	\$ 5,867,732.38
The Contract Time will be increased by	(201) Days
The Date of Completion including this Change Order therefore is	8/21/2024

EXECUTION OF THIS CHANGE ORDER ACKNOWLEDGES FINAL SETTLEMENT OF, AND RELEASE OF ALL CLAIMS FOR COSTS AND TIME ASSOCIATED, DIRECTLY OR INDIRECTLY, WITH THE ABOVE-STATED MODIFICATION(S), INCLUDING ALL CLAIMS FOR CUMULATIVE DELAYS OR DISRUPTIONS RESULTING FROM, CAUSED BY, OR INCIDENT TO, SUCH MODIFICATION(S), AND INCLUDING ANY CLAIM THAT THE ABOVE-STATED MODIFICATION(S) CONSTITUTES, IN WHOLE OR PART, A CARDINAL CHANGE TO THE CONTRACT.

R&D Paving, LLC
 CONTRACTOR
 400 Executive Center Dr. Suite 210
 Address
 West Palm Beach, FL 33401

NAME: Nancy G. Rasso
 SIGNATURE: [Signature]
 TITLE: Managing Member
 DATE: 6/4/24



S/WBE - M/WBE
400 EXECUTIVE CENTER DR. STE 210
WEST PALM BEACH, FL 33401
(561) 588-6681
Fax (561) 284-6541

CO NO. 6R - Material Delays

February 28, 2023

To: Palm Beach County
2300 North Jog Rd
West Palm Beach, FL 33411

Project: Lyons Road/Sansbury's Way
Buffered Bike Lanes
Project #: 2019604

R & D Paving is requesting an extension of time due to material delays for the 4" & 8" FM.
Additional information below.

Notification from Supplier: Thursday, December 8, 2022
Notice to Proceed: Monday, February 6, 2023
Material Delivery: Tuesday, May 16, 2023

Additional Days Requested: 99 Days

Matthew M. Donnell
Project Manager

In accordance with the Contract, the undersigned certifies under oath and in writing, that the request is made in good faith, that any supportive data submitted is accurate and complete to R & D Paving's best knowledge and belief, and that the amount of the request accurately reflects what R & D Paving in good faith believes to be Palm Beach County's responsibility.

Contractor's Representative

6/4/24
Date

Nancy G. Rosso, Managing Member


STATE OF FLORIDA
COUNTY OF Palm Beach

The foregoing instrument was acknowledged before me by means of physical presence or online notarization, this 4 day of June, 2024, by Nancy G. Rosso as Managing Member for R & D Paving, on behalf of the (title of officer/member/partner) (name of corporation/company/partnership)

LLC, who is personally known to me or has produced _____ as identification. corporation/company/partnership

(Signature of Notary Public - State of Florida)

Alexandra Cortes



Chuck Cameron

From: Tiffany Cochran <Tiffany.Cochran@US-Pipe.com>
Sent: Wednesday, December 7, 2022 10:36 AM
To: Sperduto, Mike; Sean Allred
Cc: Webster, Don; Matta Jr, Jim
Subject: RE: [EXTERNAL] DIP lead time

CAUTION: External

8" ETA April 2024

4" ETA FEB 2024

Best Regards,
Tiffany



Tiffany Cochran
Customer Service Representative

2023 St. Louis Avenue
Bessemer, AL 35020
T 205.417-8420

tiffany.cochran@us-pipe.com

From: Sperduto, Mike <Mike.Sperduto@coreandmain.com>
Sent: Wednesday, December 7, 2022 9:16 AM
To: Sean Allred <sallred@uspipe.com>; Tiffany Cochran <Tiffany.Cochran@US-Pipe.com>
Cc: Webster, Don <Don.Webster@coreandmain.com>; Matta Jr, Jim <James.Matta@coreandmain.com>
Subject: [EXTERNAL] DIP lead time

CAUTION: This email originated from outside of the organization. Exercise caution when opening attachments or clicking links, especially from *UNKNOWN* senders.

Good Morning,

Would US Pipe be able to provide a letter estimating lead times for this pipe please?

1,320' of 4" CL350 DIP P401 and 2,460' of 8" CL350 DIP P401 lined pipe

Thank You,
Mike Spurduto

Branch Operations Manager
Core & Main, LP
1101 West 17th Street
Riviera Beach, FL 33404
P 561-848-4396
F 561-845-7267
C 561-253-5964

*****Please Remit Payments to*****

Core & Main, LP
PO Box 28330
St. Louis, MO 63146



Core and Main is the embodiment of Dependable Expertise. The name evokes strength and dependability. "Core" represents the infrastructure that is the core of our communities, the customers who are the core of our business and the values that are the core of our culture. "Main," represents our commitment to providing the fundamental materials for waterworks, fire protection and fusible piping, as well as our commitment to Main Streets everywhere.

This message is for intended addressee(s) only and may contain confidential, proprietary or privileged information, exempt from disclosure, and subject to terms at: <http://emailterms.coreandmain.com>.



Two Chase Corporate Drive
Suite 200
Birmingham, Alabama 35244

May 21st, 2024

Mr. Mike Spurduto
Core & Main- West Palm
1101 W 17th St
Riviera Beach, FL 33404

RE: Pipe deliveries for Lyons Rd and Sansbury -West Palm Beach, FL (Johnson Davis Inc)
Core & Main PO# 1155506
Ref: U.S. Pipe Quote # 294625

Dear Mr. Spurduto,

As seen with many other material suppliers in this industry during this time, U.S. Pipe experienced unprecedented demand for its products, which was the cause for extended lead-times associated with this order. We received your purchase order on 1/13/23 and had an estimated lead-time of 16-20 weeks for this material based on current backlog. Our records indicate that this material shipped to Johnson Davis during the week of May 9th, 2023.

I am happy to report that lead-times have normalized. Should you have any further questions, please feel free to reach out to me at (407) 592-1175.

Respectfully,


Todd Lewis
Director of Sales- Southeast



INVOICE

1830 Craig Park Court
St. Louis, MO 63146

Invoice # 8871622
Invoice Date 5/17/23
Account # 015329
Sales Rep DON WEBSTER
Phone # 561-848-4396
Branch #039 Riviera Beach, FL
Total Amount Due \$56,716.36

Backordered from:
5/17/23 S216562

Remit To:
CORE & MAIN LP
PO BOX 28330
ST. LOUIS, MO 63146

JOHNSON-DAVIS INC
604 HILLBRATH DR
LANTANA FL 33462-1656

000/0000
00000

Shipped To:
SANDBURY WAY BUFFERED BIKE
LANES (PROJ #2019604)
WEST PALM BEACH, FL

CUSTOMER JOB- JD32031 LYONS RD/SANSE LYONS SANBURY

Thank you for the opportunity to serve you! We appreciate your prompt payment.

Date Ordered	Date Shipped	Customer PO #	Job Name	Job #	Bill of Lading	Shipped Via	Invoice#
1/13/23	5/16/23	32031.002	LYONS RD/SANSE	JD32031		DIRECT	8871622

Product Code	Description	Quantity		B/O	Price	UM	Extended Price
		Ordered	Shipped				
0108350TP401	CORE & MAIN PO#- 8 TJ PR350 DI PIPE P401	1155506	863	863	62.00000	FT	53,506.00

Freight	Delivery	Handling	Restock	Misc	Subtotal:	53,506.00
					Other:	.00
					Tax:	3,210.36
Invoice Total:						\$56,716.36

Terms: NET 30
Ordered By: CHAD

This transaction is governed by and subject to Core & Main's standard terms and conditions, which are incorporated by reference and accepted.
To review these terms and conditions, please visit: <http://tandc.coreandmain.com/>

00000



INVOICE

1830 Craig Park Court
St. Louis, MO 63146

Invoice # 8216562
Invoice Date 5/17/23
Account # 015329
Sales Rep DON WEBSTER
Phone # 561-848-4396
Branch #039 Riviera Beach, FL
Total Amount Due \$181,960.84

Remit To:
CORE & MAIN LP
PO BOX 28330
ST. LOUIS, MO 63146

JOHNSON-DAVIS INC 000/0000
604 HILLBRATH DR 00000
LANTANA FL 33462-1656

Shipped To:
SANDBURY WAY BUFFERED BIKE
LANES (PROJ #2019604)
WEST PALM BEACH, FL

CUSTOMER JOB- JD32031 LYONS RD/SANSB LYONS SANDBURY

Thank you for the opportunity to serve you! We appreciate your prompt payment.

Date Ordered	Date Shipped	Customer PO #	Job Name	Job #	Bill of Lading	Shipped Via	Invoice#
1/13/23	5/16/23	32031.002	LYONS RD/SANSB	JD32031		DIRECT	S216562

Product Code	Description	Quantity			Price	UM	Extended Price
		Ordered	Shipped	B/O			
	CORE & MAIN PO#-	1155506					
0104350TP401	4 TJ PR350 DI PIPE P401	1320	1320		55.00000 FT	72,600.00	
0108350TP401	8 TJ PR350 DI PIPE P401	2460	1597	863	62.00000 FT	99,014.00	

Freight	Delivery	Handling	Restock	Misc	Subtotal:	171,614.00
					Other:	.00
					Tax:	10,346.84
Terms: NET 30 Ordered By: CHAD					Invoice Total:	\$181,960.84

This transaction is governed by and subject to Core & Main's standard terms and conditions, which are incorporated by reference and accepted.
To review these terms and conditions, please visit: <http://tandc.coreandmain.com/>

00000



INVOICE

1830 Craig Park Court
St. Louis, MO 63146

Invoice # 8216576
Invoice Date 8/15/23
Account # 015329
Sales Rep DON WEBSTER
Phone # 561-848-4396
Branch #039 Riviera Beach, FL
Total Amount Due \$2,311.20

Remit To:
CORE & MAIN LP
PO BOX 28330
ST. LOUIS, MO 63146

JOHNSON-DAVIS INC 000/0000
604 HILLBRATH DR 00000
LANTANA FL 33462-1656

Shipped To:
SANDBURY WAY BUFFERED BIKE
LANES (PROJ #2019604)
WEST PALM BEACH, FL

CUSTOMER JOB- JD32031 LYONS RD/SANSB LYONS SANDBURY

Thank you for the opportunity to serve you! We appreciate your prompt payment.

Date Ordered 1/13/23 Date Shipped 5/08/23 Customer PO # 32031.002 Job Name LYONS RD/SANSB Job # JD32031 Bill of Lading Shipped Via CORE & MAIN LP Invoice# S216576

Product Code	Description	Quantity		Price	UM	Extended Price
		Ordered	Shipped			
010650TP401	6 TJ CL50 PR350 DI PIPE P401	20	20	✓ 46.00000	FT	920.00
0108350TP401	8 TJ PR350 DI PIPE P401	20	20	✓ 62.00000	FT	1,240.00

Handwritten notes and signatures:
8/18/23
CHAD

243 203
870.00

Proof of Delivery
Signed by: CHAD
JOHNSON-DAVIS INC
08/14/2023 10:43

Freight Delivery Handling Restock Misc

Subtotal: 2,160.00
Other: 179.60
Tax: 55.20

Terms: NET 30
Ordered By: CHAD

Invoice Total: 2381.80 ~~2,311.20~~

This transaction is governed by and subject to Core & Main's standard terms and conditions, which are incorporated by reference and accepted. To review these terms and conditions, please visit: <http://tancc.coreandmain.com/>



S/WBE - M/WBE
400 EXECUTIVE CENTER DR. STE 210
WEST PALM BEACH, FL 33401
(561) 588-6681
Fax (561) 284-6541

CO NO. 17R - MCI Conflict Delay Days

February 14, 2024

To: Palm Beach County
2300 North Jog Rd
West Palm Beach, FL 33411

Project: Lyons Road/Sansbury's Way
Buffered Bike Lanes
Project #: 2019604

R & D Paving is requesting time and compensation due to MCI Conflict. Additional information below.

Delay Days: 102 Days
Conflict: Monday, September 18, 2023
Conflict Resolved: Tuesday, January 9, 2024

Matthew M. Donnell
Project Manager

In accordance with the Contract, the undersigned certifies under oath and in writing, that the request is made in good faith, that any supportive data submitted is accurate and complete to R & D Paving's best knowledge and belief, and that the amount of the request accurately reflects what R & D Paving in good faith believes to be Palm Beach County's responsibility.

[Signature] 6/4/24
Contractor's Representative Date

Nancy G. Rosso, Managing Member

STATE OF FLORIDA
COUNTY OF Palm Beach


The foregoing instrument was acknowledged before me by means of physical presence or online notarization, this 4 day of June, 2024, by Nancy G. Rosso

as Managing Member for R & D Paving,, on behalf of the
(title of officer/member/partner) (name of corporation/company/partnership)

LLC, who is personally known to me or has produced _____ as identification.
corporation/company/partnership

(Signature of Notary Public - State of Florida)

[Signature]
Alexandra Cortes





S/WBE – M/WBE
400 EXECUTIVE CENTER DRIVE, STE 210
WEST PALM BEACH, FL 33401
(561) 588-6681
Fax (561) 284-6541
office@randdpaving.com

Date: December 13, 2023

To: Palm Beach County
Construction Coordination
PO Box 21229
West Palm Beach, FL 33416

Project: Lyons Road/Sansbury's Way Buffered Bike Lanes

Re: Notice of Intent

On September 18th, JD came into conflict with MCI/Verizon and all work had to be stopped, no further work can be completed until this line is relocated.

R & D Paving is hereby notifying you of our Notice of Intent to Claim for the preservation, presentation and resolution of the claim for time and compensation regarding the MCI/Verizon conflict and resulting delays. Once relocated, R & D Paving will provide an official change order for time and compensation.

Please let me know if you have any questions or require any further information.

Respectfully,

Nancy G. Rosso
Managing Member



Matt Donnell <matt@randdpaving.com>

FW: FW: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

1 message

Trent Liguori <tliguori@bcceng.com>
To: "matt@randdpaving.com" <matt@randdpaving.com>
Cc: "Andre H. Thomas" <athomas@bcceng.com>, Zachary King <ZKing@pbcgov.org>

Tue, Jan 9, 2024 at 12:42 PM

Matt,

Please see the confirmation below regarding the remaining MCI conduit on the Lyons project.

Thanks,

Trent Liguori, PE

CEI Project Administrator



t. 561.655.0655 | m. 754.276.6739 | www.bcceng.com

From: Brad Shults <brads@cwsifl.com>
Sent: Tuesday, January 9, 2024 12:39 PM
To: Trent Liguori <tliguori@bcceng.com>
Cc: Andre H. Thomas <athomas@bcceng.com>
Subject: RE: FW: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Yes, confirmed.



Brad Shults

Director of Business Operations

Cable Wiring Specialists Inc.

5900 Mayo Street, Hollywood FL 33023

(O)954-893-0501 ext 208

(F)954-893-0448

© 239-633-4360

From: Trent Liguori <tliguori@bcceng.com>

Sent: Tuesday, January 9, 2024 12:13 PM

To: Brad Shults <brads@cwsifl.com>

Cc: Andre H. Thomas <athomas@bcceng.com>

Subject: FW: FW: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

You don't often get email from tliguori@bcceng.com. Learn why this is important

Good morning Brad,

Can you please confirm that the contractor on the PBC project will not be responsible for damage to the conduit left in place.

We will provide notice as best as possible of any damage identified so that MCI can repair on their own accord.

Thanks,

Trent Liguori, PE

CEI Project Administrator



t. 561.655.0655 | m. 754.276.6739 | www.bcceng.com

From: Matt Donnell <matt@randdpaving.com>
Sent: Wednesday, January 3, 2024 2:36 PM
To: Trent Liguori <tliguori@bcceng.com>
Cc: Zachary King <ZKing@pbcgov.org>; Andre H. Thomas <athomas@bcceng.com>
Subject: Re: FW: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Trent

I will need a letter from the owner stating that R & D Paving and its subcontractors hold no responsibility to any costs associated with any damage to the conduit/ducts.

Thank you,

Matthew M. Donnell

Estimator

400 Executive Center Dr, Suite 210

West Palm Beach, FL 33401

O: (561) 588-6681 C: (561) 718-4460



On Wed, Jan 3, 2024 at 2:28 PM Trent Liguori <tliguori@bcceng.com> wrote:

Matt,

As noted below by MCI's contractor, the fiber has been removed along the fairgrounds. Please proceed with the work in the area accordingly and advise if any portion of the conduit remaining is damaged, so the CWSI can repair as a future spare.

Thanks,

Trent Liguori, PE

CEI Project Administrator



GETTING THERE
JUST GOT EASIER™

t. 561.655.0655 | m. 754.276.6739 | www.bcceng.com

From: Brad Shults <brads@cwsifl.com>
Sent: Wednesday, January 3, 2024 2:21 PM
To: Trent Liguori <tliguori@bcceng.com>
Cc: donovan.carr@verizon.com; Jeffrey Mogell <jeffreym@cwsifl.com>; Andre H. Thomas <athomas@bcceng.com>
Subject: RE: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Yes we removed the fiber can you let us know if you hit the duct so we can repair



Brad Shults
Director of Business Operations

Cable Wiring Specialists Inc.
5900 Mayo Street, Hollywood FL 33023
(O)954-893-0501 ext 208
(F)954-893-0448
© 239-633-4360

From: Trent Liguori <tliguori@bcceng.com>
Sent: Wednesday, January 3, 2024 12:54 PM
To: Brad Shults <brads@cwsifl.com>
Cc: donovan.carr@verizon.com; Jeffrey Mogell <jeffreym@cwsifl.com>; Andre H. Thomas <athomas@bcceng.com>
Subject: RE: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Some people who received this message don't often get email from tliguori@bcceng.com. Learn why this is important

Hi Brad,

Following up on this work. It's my understanding that there were crews working on this yesterday. Can you advise if the work to pull the cable from the conduit was complete?

Thanks,

Trent Liguori, PE

CEI Project Administrator



GETTING THERE
JUST GOT EASIER

t. 561.655.0655 | m. 754.276.6739 | www.bcceng.com

From: Andre H. Thomas <athomas@bcceng.com>

Sent: Friday, December 22, 2023 10:02 AM

To: Matt Donnell <matt@randdpaving.com>

Cc: Zachary King <ZKing@pbcgov.org>; Brad Shults <brads@cwsifl.com>; Trent Liguori <tliguori@bcceng.com>; Dave West <DWest1@pbcgov.org>; donovan.carr@verizon.com; Jeffrey Mogell <jeffreym@cwsifl.com>; Albert Hoffman <AWHoffman@pbcgov.org>

Subject: Re: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Matt,

We are waiting to hear back from Brad. In the field we discussed with Kevin staging locations and MOT. I would figure once locates are completed MCI/Verizon's contractor will be able to schedule crews and I will let Brad answer that question. Just so everyone is aware no work can be performed between Jan 12-28 due to the South Florida Fair in that area. This leaves the window to complete this work between 12/28 through 1/11.

Regards,

Andre H. Thomas, PE

CEI Senior Project Engineer



GETTING THERE
JUST GOT EASIER™

700 N. Olive Ave, Suite 1, West Palm Beach, FL 33401

t. 561.655.0655 | m. 561.657.1973 | www.bcceng.com



From: Matt Donnell <matt@randdpaving.com>
Sent: Friday, December 22, 2023 9:57:25 AM
To: Andre H. Thomas <athomas@bcceng.com>
Cc: Zachary King <ZKing@pbcgov.org>; Brad Shults <brads@cwsifl.com>; Trent Liguori <tliguori@bcceng.com>; Dave West <DWest1@pbcgov.org>; donovan.carr@verizon.com <donovan.carr@verizon.com>; Jeffrey Mogeli <jeffreym@cwsifl.com>; Albert Hoffman <AWHoffman@pbcgov.org>
Subject: Re: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Andre,

Do you have an update from yesterday's meeting?

Thank you,

Matthew M. Donnell

Estimator

400 Executive Center Dr, Suite 210

West Palm Beach, FL 33401

O: (561) 588-6681 C: (561) 718-4460



On Thu, Dec 21, 2023 at 11:55 AM Andre H. Thomas <athomas@bcceng.com> wrote:

Team,

I will be meeting with CWSI in the field today around 1:00pm to discuss the scope of work needed to be completed to relocate the line between STA 427+00 to STA 434+00.

Thank you Brad for your prompt response.

Andre H. Thomas, PE

CEI Senior Project Engineer



t. 561.655.0655 | www.bcceng.com

From: Zachary King <ZKing@pbcgov.org>
Sent: Friday, December 15, 2023 2:31 PM
To: Matt Donnell <matt@randdpaving.com>; Brad Shults <brads@cwsifl.com>; Trent Liguori <tliguori@bcceng.com>; Andre H. Thomas <athomas@bcceng.com>; Dave West <DWest1@pbcgov.org>; donovan.carr@verizon.com
Cc: Jeffrey Mogell <jeffreym@cwsifl.com>; Albert Hoffman <AWHoffman@pbcgov.org>
Subject: RE: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Donovan,

Please see attached R&D's letter of intent to claim for time and compensation due to delays caused by the Verizon/MCI conflict. Please get us some sort of update regarding the relocation status of this line. Work can no longer progress within this area due to the conflict and Verizon's lack of response is now costing the county money. If Verizon could please expedite this relocation it would be greatly appreciated by the County.

From: Matt Donnell <matt@randdpaving.com>
Sent: Tuesday, November 14, 2023 12:41 PM
To: Brad Shults <brads@cwsifl.com>; Zachary King <ZKing@pbcgov.org>; Trent Liguori <tliguori@bcceng.com>; Andre Thomas <athomas@bcceng.com>; Dave West <DWest1@pbcgov.org>
Cc: Carr, Donovan Ralph <donovan.carr@verizon.com>; Jeffrey Mogell <jeffreym@cwsifl.com>
Subject: Re: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Brad/Donovan,

Do you have an update on this conflict? We are going on 2 months since we notified you of the conflict and do not have any answers on a date or plan going forward.

Thank you,

Matthew M. Donnell

Estimator

400 Executive Center Dr, Suite 210 [maps.google.com]

West Palm Beach, FL 33401 [maps.google.com]

O: (561) 588-6681 C: (561) 718-4460

[Redacted]

On Tue, Oct 31, 2023 at 2:30 PM Matt Donnell <matt@randdpaving.com> wrote:

A month ago when we found the conflict.

Matthew M. Donnell

Estimator

400 Executive Center Dr, Suite 210 [maps.google.com]

West Palm Beach, FL 33401 [maps.google.com]

O: (561) 588-6681 C: (561) 718-4460

[Redacted]

On Tue, Oct 31, 2023 at 2:28 PM Brad Shults <brads@cwsifl.com> wrote:

Matt

Thank you for the conflict matrix do you have a estimated time you need to have this moved?

2340428 - TBD - MCI Conflict @ Sansbury's Way



Brad Shults

Director of Business Operations

Cable Wiring Specialists Inc.

5900 Mayo Street, Hollywood FL 33023

(O)954-893-0501 ext 208

(F)954-893-0448

© 239-633-4360

From: Matt Donnell <matt@randdpaving.com>

Sent: Tuesday, October 31, 2023 11:46 AM

To: Brad Shults <brads@cwsifl.com>

Cc: Carr, Donovan Ralph <donovan.carr@verizon.com>; Jeffrey Mogell <jeffreym@cwsifl.com>

Subject: Re: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Please see attached.

Matthew M. Donnell

Estimator

400 Executive Center Dr, Suite 210 [maps.google.com]

West Palm Beach, FL 33401 [maps.google.com]

O: (561) 588-6681 **C:** (561) 718-4460

On Fri, Oct 27, 2023 at 7:59 AM Brad Shults <brads@cwsifl.com> wrote:

Matt

Thank you for taking my call today. If you can send me the drawings for this conflict area for the Verizon/MCI fiber that is in conflict I will have someone there next week to see if we can resolve the issue.

Jeff

Please open a relocation project for Donovan



Brad Shults
Director of Business Operations

Cable Wiring Specialists Inc.
5900 Mayo Street, Hollywood FL 33023
(O)954-893-0501 ext 208
(F)954-893-0448
© 239-633-4360

From: Carr, Donovan Ralph <donovan.carr@verizon.com>
Sent: Thursday, October 26, 2023 2:00 PM
To: Brad Shults <brads@cwsifl.com>
Subject: Fwd: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Hey Brad,

Please see the email from Matt Donnell. We have a conduit on Sansbury's Way in WPB (just north of the recent damage) that is apparently in conflict. Can you help with this?

Thanks,

Donovan Carr
Engr III Spec-Ntwk Eng&Ops

4700 Exchange Ct
Boca Raton, FL 33431

Cell: 954-213-1959
Jabber: 910-969-6210

----- Forwarded message -----

From: Matt Donnell <matt@randdpaving.com>

Date: Fri, Oct 20, 2023 at 3:26 PM

Subject: Re: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

To: Carr, Donovan Ralph <donovan.carr@verizon.com>, Zachary King <zking@pbcgov.org>, Trent Liguori <tliguori@bcceng.com>, Andre Thomas <athomas@bcceng.com>, Dave West <dwest1@pbcgov.org>

Donovan,

Do you have an update? It has now been a month since we confirmed the conflicting line.

Matthew M. Donnell

Estimator

400 Executive Center Dr, Suite 210

West Palm Beach, FL 33401

O: (561) 588-6681 C: (561) 718-4460

On Tue, Oct 17, 2023 at 11:35 AM Matt Donnell <matt@randdpaving.com> wrote:

Please see link.

Final Roadway Plans S&S 10.11.2023.pdf

Matthew M. Donnell

Estimator

EXHIBIT "B" (Page 18 of 25)

400 Executive Center Dr, Suite 210

West Palm Beach, FL 33401

O: (561) 588-6681 C: (561) 718-4460

[Redacted]

On Mon, Oct 16, 2023 at 8:45 AM Carr, Donovan Ralph <donovan.carr@verizon.com> wrote:

Matt,

Could you possibly send me a copy of your plans?

Thanks,

[Redacted]

Donovan Carr
Engr III Spec-Ntwk Eng&Ops

4700 Exchange Ct
Boca Raton, FL 33431

Cell: 954-213-1959
Jabber: 910-969-6210

On Fri, Sep 29, 2023 at 8:26 AM Matt Donnell <matt@randdpaving.com> wrote:

Donovan,

The line is in conflict with the proposed drainage.

Sent from my iPhone

Begin forwarded message:

From: Dennis Torrijos <Dennis.Torrijos@mastec.com>

Date: September 26, 2023 at 5:44:58 PM EDT

To: matt@randdpaving.com

Subject: FW: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Hello Matt. I was forwarded this email from Verizon. I can make it out tomorrow morning to see what's going on here on behalf of Donovan.

Will you be on site tomorrow?

Regards,



Dennis Torrijos
Construction Manager
MasTec Communications
Group
M: (954) 235-3605
Dennis.Torrijos@MasTec.com
| www.MasTec.com

From: Carr, Donovan Ralph <donovan.carr@verizon.com>
Sent: Tuesday, September 26, 2023 12:08 PM
To: Greg Arguez <Greg.Arguez@mastec.com>
Subject: [External] Fwd: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict

Greg,

Please take a look at the email from Matt Donnell.

Thanks,

Donovan Carr
Engr III Spec-Ntwk Eng&Ops

4700 Exchange Ct
Boca Raton, FL 33431

Cell: 954-213-1959
Jabber: 910-969-6210

----- Forwarded message -----

From: Carr, Donovan Ralph <donovan.carr@verizon.com>
Date: Mon, Sep 25, 2023 at 2:08 PM
Subject: Re: [E] Re: PBC Lyons Road and Sansbury's Way - MCI Conflict
To: Matt Donnell <matt@randdpaving.com>

Matt,

I'm at a doctors appointment. I'll call you ASAP.

Thanks,

Donovan Carr

On Mon, Sep 25, 2023 at 2:06 PM Matt Donnell <matt@randdpaving.com> wrote:

Donovan,

I have tried to call you back a few times with no luck. Can you confirm if this is your line and what we need to do to move forward with having it relocated?

Thank you,

Matthew M. Donnell

Estimator

400 Executive Center Dr, Suite 210

West Palm Beach, FL 33401

O: (561) 588-6681 C: (561) 718-4460

On Thu, Sep 21, 2023 at 9:46 AM Matt Donnell <matt@randdpaving.com> wrote:

Donovan,

We have located what we believe is one of your lines that is in conflict with construction. Please see attached plan sheets and a picture of the exposed line. The line in question is located on Sansbury's way on the West side of the road in front of the Ithink Financial Amphitheatre. Can you please confirm this is yours and let me know what we need to do to move forward with relocating this line. Do not hesitate to call me with any questions or concerns.

Thank you,

Matthew M. Donnell

Estimator

400 Executive Center Dr, Suite 210

West Palm Beach, FL 33401

O: (561) 588-6681 C: (561) 718-4460

Under Florida law, e-mail addresses are public records. If you do not want your e-mail address released in response to a public records request, do not send electronic mail to this entity. Instead, contact this office by phone or in writing.



image015.png
14K

Zachary King

From: Alvarez, Ramon <Ramon.Alvarez@dot.state.fl.us>
Sent: Monday, March 11, 2024 4:21 PM
To: Zachary King; McLellan, John
Cc: Alexis Burrie
Subject: RE: 2019604 Lyons Road/Sansbury's FM#444370-1-58-01 Verizon Delay

This Message Is From an External Sender

This message came from outside your organization.

Zach,

The LAP Office concurs with the CO at no additional cost to the Department.

Thank you,

-Ramon E. Alvarez
FDOT D4 LAP Coordinator
(954) 777-4403
M-F – 8:30AM-5:30PM

From: Zachary King <ZKing@pbcgov.org>
Sent: Monday, March 11, 2024 3:20 PM
To: McLellan, John <John.McLellan@dot.state.fl.us>
Cc: Alexis Burrie <aburrie@aeengineeringinc.com>; Alvarez, Ramon <Ramon.Alvarez@dot.state.fl.us>
Subject: RE: 2019604 Lyons Road/Sansbury's FM#444370-1-58-01 Verizon Delay

Thanks

From: McLellan, John <John.McLellan@dot.state.fl.us>
Sent: Monday, March 11, 2024 3:06 PM
To: Zachary King <ZKing@pbcgov.org>
Cc: Alexis Burrie <aburrie@aeengineeringinc.com>; Alvarez, Ramon <Ramon.Alvarez@dot.state.fl.us>
Subject: RE: 2019604 Lyons Road/Sansbury's FM#444370-1-58-01 Verizon Delay

Thank you. I agree with the 102 days. Combined with what was previously submitted, this CO should be acceptable.

John McLellan
LAP Coordinator
FDOT District 4, Palm Beach Operations Center
7900 Forest Hill Blvd, West Palm Beach, FL 33413
Cell: (561) 764-7284 | Office: (561) 370-1216



[fdot.gov]

JOB ITEM #111 FOR DELAY W/ MILESTONE - J

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Dec 11, '22									
								W	T	F	S	S	M	T	W	T	
1	★	Notification from Fortline & Core & Main of Pipe Delivery Delay	114 days	Thu 12/8/22	Tue 5/16/23												
2	★	Mobilization	259 days	Mon 2/6/23	Thu 2/1/24												
3	★	MOT	259 days	Mon 2/6/23	Thu 2/1/24												
4	★	Phase IA(Station 315+82 to 345+00) Southbound	128 days	Wed 3/22/23	Fri 9/15/23												
5	★	MOT	102 days	Wed 3/22/23	Thu 8/10/23												
6	✓ ★	Clearing and Grubbing	85 days	Wed 3/22/23	Tue 7/18/23												
7	✓ ★	Regular Excavation/Embankment	25 days	Wed 4/19/23	Tue 5/23/23												
8	✓ ★	Subsoil Excavation	65 days	Wed 4/19/23	Tue 7/18/23												
9	✓ ★	Optional Base Group 13	25 days	Wed 4/19/23	Tue 5/23/23												
10	✓ ★	Superpave Asphalt Concrete(Widening)	7 days	Wed 5/24/23	Thu 6/1/23	9											
11	✓ ★	Concrete Sidewalks & Driveways	41 days	Fri 5/26/23	Fri 7/21/23												
12	✓ ★	Concrete Curbing	41 days	Fri 5/26/23	Fri 7/21/23												
13	✓ ★	Grade Swales	35 days	Mon 6/5/23	Fri 7/21/23												
14	✓ ★	Sod	20 days	Mon 7/10/23	Fri 8/4/23												
15	✓ ★	Milling(Concrete Separator)	4 days	Mon 8/7/23	Thu 8/10/23	14											
16	✓ ★	Concrete Separator	21 days	Fri 8/11/23	Fri 9/8/23	15											
17	★	Final Lift Asphalt(Widening)	5 days	Mon 9/11/23	Fri 9/15/23	16											

Project: Lyons Road Sansburrys
Date: Wed 2/14/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

EXHIBIT 27 (page 2 of 15)

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Dec 11, '22									
								W	T	F	S	S	M	T	W	T	
18		Phase IB(Station 315+82 to 345+00) Northbound	156 days	Tue 5/30/23	Tue 1/2/24												
19		MOT	130 days	Tue 5/30/23	Mon 11/27/2												
20		Clearing and Grubbing	61 days	Tue 5/30/23	Tue 8/22/23												
21		Regular Excavation/Embankment	51 days	Mon 6/5/23	Mon 8/14/23												
22		Optional Base Group 13	27 days	Mon 6/5/23	Tue 7/11/23												
23		Optional Base Group 2	27 days	Mon 6/5/23	Tue 7/11/23												
24		Superpave Asphalt Concrete(Widening)	2 days	Wed 7/12/23	Thu 7/13/23	23											
25		Concrete Sidewalks & Driveways	30 days	Wed 6/28/23	Tue 8/8/23												
26		Concrete Curbing	2 days	Mon 7/31/23	Tue 8/1/23												
27		Grade Swales	35 days	Fri 7/14/23	Thu 8/31/23	24											
28		Sod	35 days	Mon 8/14/23	Fri 9/29/23												
29		Milling(Concrete Separator)	4 days	Mon 10/2/23	Thu 10/5/23	28											
30		Concrete Separator	21 days	Fri 10/6/23	Fri 11/3/23	29											
31		Final Lift Asphalt(Widening)	5 days	Mon 11/6/23	Fri 11/10/23	30											
32		Milling(Mainline Transitions)	5 days	Mon 11/13/23	Fri 11/17/23	31											
33		Final Lift Asphalt	5 days	Mon 11/20/23	Fri 11/24/23	32											
34		Asphalt Cure Period	21 days	Mon 11/27/23	Mon 12/25/23	33											
35		Final Striping/Signage	6 days	Tue 12/26/23	Tue 1/2/24	34											

Project: Lyons Road Sansburrys
Date: Wed 2/14/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Dec 11, '22									
								W	T	F	S	S	M	T	W	T	
36		Phase IIA(Station 423+68.51 to 440+30.77)Southbound	269 days?	Wed 6/28/23	Mon 7/8/24												
37		MOT	63 days	Mon 5/15/23	Wed 8/9/23												
38	✓	Clearing and Grubbing(Concrete)	5 days	Mon 5/15/23	Fri 5/19/23												
39	✓	4" FM	15 days	Mon 6/19/23	Fri 7/7/23												
40	✓	Pressure Test	1 day	Mon 7/10/23	Mon 7/10/23	39											
41	✓	FM Connection Delay	40 days	Wed 7/26/23	Tue 9/19/23												
42	✓	Connection	1 day	Wed 9/20/23	Wed 9/20/23	41											
43	✓	Clearing and Grubbing(FM)	7 days	Thu 9/21/23	Fri 9/29/23	42											
44	✓	Drainage Conflict(MCI)	82 days	Mon 9/18/23	Tue 1/9/24												
45	✓	South Florida Fair	12 days	Fri 1/12/24	Sun 1/28/24												
46		Drainage Installation	18 days	Mon 1/29/24	Wed 2/21/24	44											
47		Excavation/Embankment	12 days	Thu 2/22/24	Fri 3/8/24	46											
48		Optional Base Group 13(First Lift)	8 days	Mon 3/11/24	Wed 3/20/24	47											
49		F Curb/Drop Curb	8 days	Thu 3/21/24	Mon 4/1/24	48											
50		Optional Base Group 13(Final Lift)	12 days	Tue 4/2/24	Wed 4/17/24	49											
51		Superpave Asphalt Concrete	5 days	Thu 4/18/24	Wed 4/24/24	50											
52		Overbuild	5 days	Thu 4/18/24	Wed 4/24/24	50											
53		Concrete Sidewalk	10 days	Thu 4/25/24	Wed 5/8/24	51											
54		Sod	5 days	Thu 5/9/24	Wed 5/15/24	53											

Project: Lyons Road Sansburrys
Date: Wed 2/14/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Dec 11, '22									
								W	T	F	S	S	M	T	W	T	
55		Concrete Traffic Separator	10 days	Tue 6/25/24	Mon 7/8/24	67											
56		Phase IIB(Station 423+68.51 to 440+30.77)Northbound	228 days	Mon 8/7/23	Wed 6/19/24												
57		MOT	37 days	Mon 8/7/23	Tue 9/26/23												
58	✓	2 ea 2" PVC Conduits	16 days	Mon 8/7/23	Mon 8/28/23												
59	✓	Electrical Pull Boxes	16 days	Mon 8/7/23	Mon 8/28/23												
60		Clearing and Grubbing	15 days	Thu 5/9/24	Wed 5/29/24	53											
61		Excavation/Embankment	18 days	Thu 5/9/24	Mon 6/3/24	53											
62		Optional Base Group 13	18 days	Thu 5/9/24	Mon 6/3/24	53											
63		F Curb	18 days	Thu 5/9/24	Mon 6/3/24	53											
64		Superpave Asphalt Concrete	5 days	Tue 6/4/24	Mon 6/10/24	62											
65		Overbuild	5 days	Tue 6/4/24	Mon 6/10/24	62											
66		Grade Swales	5 days	Tue 6/11/24	Mon 6/17/24	65											
67		Sod	5 days	Tue 6/18/24	Mon 6/24/24	66											
68		Concrete Traffic Separator	10 days	Tue 6/25/24	Mon 7/8/24	67											
69		Milling	5 days	Tue 7/9/24	Mon 7/15/24	68											
70		Final Lift Asphalt	5 days	Tue 7/9/24	Mon 7/15/24	68											
71		Cure Period	16 days	Tue 7/16/24	Tue 8/6/24	70											
72		Striping/Signage	2 days	Wed 8/7/24	Thu 8/8/24	71											
73		Phase IIIA(Station 458+7.28 to 516+76)Southbound	204 days	Wed 6/28/23	Mon 4/8/24												
74		8" FM Material Delay	114 days	Thu 12/8/22	Tue 5/16/23												
75		MOT	167 days	Wed 6/28/23	Thu 2/15/24												

Project: Lyons Road Sansburrys
Date: Wed 2/14/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

EXHIBIT B (Pages 2 of 15)

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Dec 11, '22									
								W	T	F	S	S	M	T	W	T	
76	✓	✈	Clearing and Grubbing(Tree Demo)	14 days	Wed 6/28/23	Mon 7/17/23											
77	✓	✈	8" FM	18 days	Wed 6/28/23	Fri 7/21/23											
78	✓	✈	Pressure Test	1 day	Mon 7/24/23	Mon 7/24/23	77										
79	✓	✈	Health Dept Delay Due to 4" FM Delay	41 days	Wed 7/26/23	Wed 9/20/23											
80	✓	✈	Connection	1 day	Thu 9/21/23	Thu 9/21/23	79										
81	✓	✈	Clearing and Grubbing(FM)	5 days	Fri 9/22/23	Thu 9/28/23	80										
82	✓	✈	Drainage	18 days	Fri 9/29/23	Tue 10/24/23	81										
83	✓	✈	Clearing and Grubbing(Concrete)	25 days	Wed 10/25/23	Tue 11/28/23	82										
84	✓	✈	Excavation/Embankment	25 days	Wed 10/25/23	Tue 11/28/23	82										
85	✓	✈	Optional Base Group 13	35 days	Wed 10/25/23	Tue 12/12/23	82										
86	✓	✈	Optional Base Group 2	35 days	Wed 10/25/23	Tue 12/12/23	82										
87	✓	✈	F Curb/Drop Curb	5 days	Mon 9/25/23	Fri 9/29/23											
88	✓	✈	Concrete Sidewalk	5 days	Mon 9/25/23	Fri 9/29/23											
89	✓	✈	Superpave Asphaltic Concrete	10 days	Wed 12/13/23	Tue 12/26/23	86										
90	✓	✈	Overbuild	10 days	Wed 12/13/23	Tue 12/26/23	86										
91	✓	✈	Grade Swales	18 days	Wed 12/27/23	Fri 1/19/24	90										
92	✓	✈	Sod	22 days	Wed 12/27/23	Thu 1/25/24	90										
93	✓	✈	Concrete Traffic Seperator	45 days	Tue 2/6/24	Mon 4/8/24	101										
94	✓	✈	Phase IIIB(Station 458+7.28 to 516+76) Northbound	154 days	Fri 11/17/23	Wed 6/19/24											

Project: Lyons Road Sansburrys Date: Wed 2/14/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Dec 11, '22									
								W	T	F	S	S	M	T	W	T	
95		MOT	55 days	Wed 12/27/2	Tue 3/12/24	89											
96		Clearing and Grubbing	18 days	Wed 12/27/2	Fri 1/19/24	89											
97		Excavation/Embankment	20 days	Wed 12/27/2	Tue 1/23/24	89											
98		Optional Base Group 13	25 days	Wed 12/27/2	Tue 1/30/24	89											
99		Optional Base Group 2	25 days	Wed 12/27/2	Tue 1/30/24	89											
100		F Curb/Drop Curb	5 days	Mon 12/4/23	Fri 12/8/23												
101		Superpave Asphaltic Concrete	4 days	Wed 1/31/24	Mon 2/5/24	99											
102		Grade Swales	12 days	Tue 2/6/24	Wed 2/21/24	101											
103		Sod	16 days	Thu 2/22/24	Thu 3/14/24	102											
104		Concrete Traffic Separator	40 days	Fri 3/15/24	Thu 5/9/24	103											
105		Milling	10 days	Fri 5/10/24	Thu 5/23/24	104											
106		Final Lift Asphalt	10 days	Fri 5/10/24	Thu 5/23/24	104											
107		Asphalt Cure Period	15 days	Fri 5/24/24	Thu 6/13/24	106											
108		Final Striping/Signage	4 days	Fri 6/14/24	Wed 6/19/24	107											

Project: Lyons Road Sansburrys
Date: Wed 2/14/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Donna Lewis

From: Angela Smith
Sent: Wednesday, March 20, 2024 3:11 PM
To: Donna Lewis
Subject: RE: Board Item (Date TBD) - Lyons Road/Sansbury's Way Buffered Bike Lanes Federalized, 2019604 - Change Order 3 - OEBO REVIEW

Hello Donna, this is a federalized contract, there is nothing for OEBO to review. Only items that have any API on them is what I should be reviewing.

Angela D. Smith
Small Business Development Specialist III
Office of Equal Business Opportunity



561-616-6840 (Main)
561-616-6852 (Direct)
561-233-2246 (E-Fax)
asmith1@pbcgov.org (email)

NOTE: Under Florida law, email addresses are public records. If you do not want your email address released in response to a public records request, do not send electronic mail to this entity. Instead, contact this office by phone or in writing.

From: Donna Lewis <DLewis1@pbcgov.org>

DESCRIPTIONS (Continued from Page 1)

Project: 2019604 Lyons Road/Sansbury's Way Buffered Bike Lanes

Palm Beach County Board of County Commissioners are additional insured with respects to General Liability, on a primary and non-contributory basis, and with regards to Auto Liability when required by written contract. Waiver of Subrogation applies in favor of additional insured with respects to General Liability, Auto Liability and Workers Compensation when required by written contract. Workers Compensation coverage for the following State(s): FL

CHANGE ORDER HISTORY

PALM BEACH COUNTY PROJECT: Lyons Road/Sansbury way Buffered Bike Lanes - Federalized, 2019604									
C.O. #	DATE APPROVED	COUNTY ENGINEER		C.R. COMMITTEE		TOTAL DEPT. & C.R.C. APPROVALS		BOARD OF CO. COMM.	
		AMOUNT	TIME	AMOUNT	TIME	AMOUNT	TIME	AMOUNT	TIME
1	10/16/2023	4,767.47	2						
2	10/27/2023	880.00	0						
3	Pending							0.00	201
	TOTAL	5,647.47	2	0.00	0	5,647.47	2		201
	CUMULATIVE TOTAL	5,647.47	2	0.00	0	5,647.47	2		
	As of PPM CW-F-050 Dated February 4, 2016	SINGLE AMT. \$50,000.00 MAX. AMT. \$250,000.00 or 5% of contract	MAX. TIME 30 DAYS	SINGLE AMT. \$100,000.00 MAX. AMT. \$250,000.00 or 5% of contract	MAX. TIME 90 DAYS	MAXIMUM CUMULATIVE CO ENG. & C.R.C. \$250,000.00 or 5% of contract	MAX. CUM. CO ENG. & C.R.C. 120 DAYS		
